




NASA SYSTEMS ENGINEERING HANDBOOK

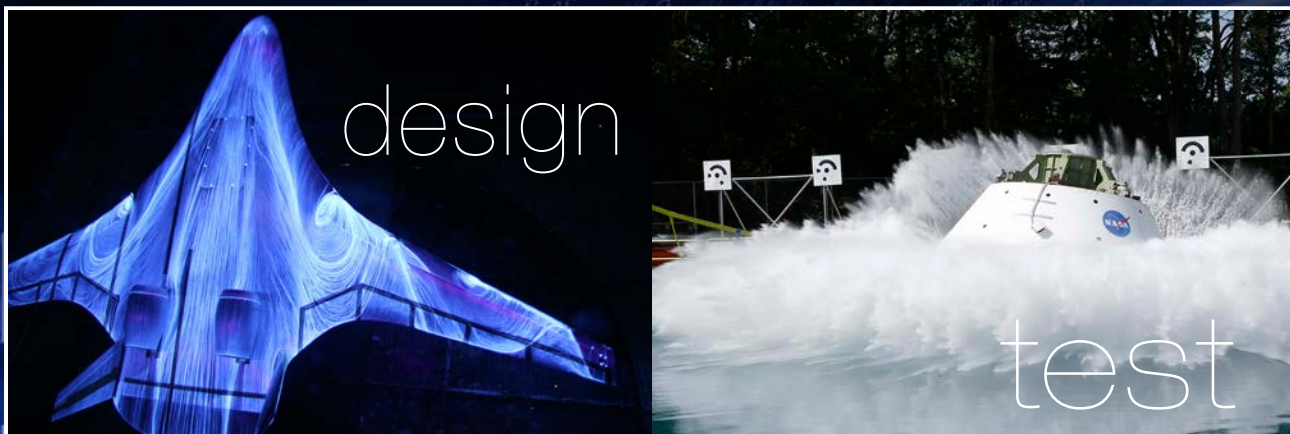

NASA SP-2016-6105 Rev2 supersedes SP-2007-6105 Rev 1 dated December, 2007.

Cover photos: *Top left:* In this photo, engineers led by researcher Greg Gatlin have sprayed fluorescent oil on a 5.8 percent scale model of a futuristic hybrid wing body during tests in the 14- by 22-Foot Subsonic Wind Tunnel at NASA's Langley Research Center in Hampton, VA. The oil helps researchers “see” the flow patterns when air passes over and around the model. (NASA Langley/Preston Martin) *Top right:* Water impact test of a test version of the Orion spacecraft took place on August 24, 2016, at NASA Langley Research Center (NASA) *Bottom left:* two test mirror segments are placed onto the support structure that will hold them. (NASA/Chris Gunn) *Bottom right:* This self-portrait of NASA's Curiosity Mars rover shows the vehicle at the “Mojave” site, where its drill collected the mission's second taste of Mount Sharp. (NASA/JPL-Caltech/MSSS)

Comments, questions, and suggestions regarding this document can be sent to:

Steven R. Hirshorn

Chief Engineer, Aeronautics Research Mission Directorate (ARMD)

Office of the Chief Engineer

NASA Headquarters, Room 6D37

300 E St SW

Washington, DC 20546-0001

202-358-0775

steven.r.hirshorn@nasa.gov

Table of Contents

<i>Preface</i>	<i>viii</i>
<i>Acknowledgments</i>	<i>ix</i>

1.0 Introduction 1

1.1 Purpose	1
1.2 Scope and Depth	1

2.0 Fundamentals of Systems Engineering 3

2.1 The Common Technical Processes and the SE Engine	5
2.2 An Overview of the SE Engine by Project Phase	8
2.3 Example of Using the SE Engine	10
2.4 Distinctions between Product Verification and Product Validation	11
2.5 Cost Effectiveness Considerations	11
2.6 Human Systems Integration (HSI) in the SE Process	12
2.7 Competency Model for Systems Engineers	13

3.0 NASA Program/Project Life Cycle 17

3.1 Program Formulation	20
3.2 Program Implementation	20
3.3 Project Pre-Phase A: Concept Studies	21
3.4 Project Phase A: Concept and Technology Development	23
3.5 Project Phase B: Preliminary Design and Technology Completion	25
3.6 Project Phase C: Final Design and Fabrication	27
3.7 Project Phase D: System Assembly, Integration and Test, Launch	29
3.8 Project Phase E: Operations and Sustainment	31
3.9 Project Phase F: Closeout	31

3.10 Funding: The Budget Cycle. 33

3.11 Tailoring and Customization of NPR 7123.1 Requirements 34

3.11.1 Introduction	34
3.11.2 Criteria for Tailoring	34
3.11.3 Tailoring SE NPR Requirements Using the Compliance Matrix	35
3.11.4 Ways to Tailor a SE Requirement	36
3.11.5 Examples of Tailoring and Customization	37
3.11.6 Approvals for Tailoring	40

4.0 System Design Processes 43

4.1 Stakeholder Expectations Definition	45
4.1.1 Process Description	45
4.1.2 Stakeholder Expectations Definition Guidance	53
4.2 Technical Requirements Definition	54
4.2.1 Process Description	54
4.2.2 Technical Requirements Definition Guidance	62
4.3 Logical Decomposition	62
4.3.1 Process Description	62
4.3.2 Logical Decomposition Guidance	65
4.4 Design Solution Definition	65
4.4.1 Process Description	66
4.4.2 Design Solution Definition Guidance	76

5.0 Product Realization 77

5.1 Product Implementation	78
5.1.1 Process Description	79
5.1.2 Product Implementation Guidance	83
5.2 Product Integration	83
5.2.1 Process Description	85
5.2.2 Product Integration Guidance	88
5.3 Product Verification	88

5.3.1	Process Description	89
5.3.2	Product Verification Guidance	99
5.4	Product Validation	99
5.4.1	Process Description	99
5.4.2	Product Validation Guidance	106
5.5	Product Transition	106
5.5.1	Process Description	106
5.5.2	Product Transition Guidance	112

6.0 Crosscutting Technical Management 113

6.1	Technical Planning	113
6.1.1	Process Description	114
6.1.2	Technical Planning Guidance	130
6.2	Requirements Management	130
6.2.1	Process Description	131
6.2.2	Requirements Management Guidance	135
6.3	Interface Management	135
6.3.1	Process Description	136
6.3.2	Interface Management Guidance	138
6.4	Technical Risk Management	138
6.4.1	Risk Management Process Description	141
6.4.2	Risk Management Process Guidance	143
6.5	Configuration Management	143
6.5.1	Process Description	144
6.5.2	CM Guidance	150
6.6	Technical Data Management	151
6.6.1	Process Description	151
6.6.2	Technical Data Management Guidance	155
6.7	Technical Assessment	155
6.7.1	Process Description	157
6.7.2	Technical Assessment Guidance	160
6.8	Decision Analysis	160
6.8.1	Process Description	164
6.8.2	Decision Analysis Guidance	170

Appendix A	Acronyms	173
Appendix B	Glossary	176
Appendix C	How to Write a Good Requirement—Checklist	197
Appendix D	Requirements Verification Matrix	201
Appendix E	Creating the Validation Plan with a Validation Requirements Matrix	203
Appendix F	Functional, Timing, and State Analysis	205
Appendix G	Technology Assessment/Insertion	206
Appendix H	Integration Plan Outline	214
Appendix I	Verification and Validation Plan Outline	216
Appendix J	SEMP Content Outline	223
Appendix K	Technical Plans	235
Appendix L	Interface Requirements Document Outline	236
Appendix M	CM Plan Outline	239
Appendix N	Guidance on Technical Peer Reviews/Inspections	240
Appendix O	Reserved	241
Appendix P	SOW Review Checklist	242
Appendix Q	Reserved	243
Appendix R	HSI Plan Content Outline	244
Appendix S	Concept of Operations Annotated Outline	251
Appendix T	Systems Engineering in Phase E	254

	References Cited	260
--	------------------	-----

	Bibliography	270
--	--------------	-----

Table of Figures

Figure 2.0-1	SE in Context of Overall Project Management	5	Figure 5.2-1	Product Integration Process	86
Figure 2.1-1	The Systems Engineering Engine (NPR 7123.1)	6	Figure 5.3-1	Product Verification Process	91
Figure 2.2-1	Miniature Version of the Poster-Size NASA Project Life Cycle Process Flow for Flight and Ground Systems Accompanying this Handbook	8	Figure 5.3-2	Example of End-to-End Data Flow for a Scientific Satellite Mission	96
Figure 2.5-1	Life-Cycle Cost Impacts from Early Phase Decision-Making	13	Figure 5.4-1	Product Validation Process	100
Figure 3.0-1	NASA Space Flight Project Life Cycle from NPR 7120.5E	18	Figure 5.5-1	Product Transition Process	107
Figure 3.11-1	Notional Space Flight Products Tailoring Process	36	Figure 6.1-1	Technical Planning Process	115
Figure 4.0-1	Interrelationships among the System Design Processes.	44	Figure 6.2-1	Requirements Management Process	131
Figure 4.1-1	Stakeholder Expectations Definition Process.	46	Figure 6.3-1	Interface Management Process.	136
Figure 4.1-2	Information Flow for Stakeholder Expectations	48	Figure 6.4-1	Risk Scenario Development.	139
Figure 4.1-3	Example of a Lunar Sortie DRM Early in the Life Cycle	51	Figure 6.4-2	Risk as an Aggregate Set of Risk Triplets.	139
Figure 4.2-1	Technical Requirements Definition Process.	55	Figure 6.4-3	Risk Management Process	141
Figure 4.2-2	Flow, Type and Ownership of Requirements.	57	Figure 6.4-4	Risk Management as the Interaction of Risk-Informed Decision Making and Continuous Risk Management	142
Figure 4.2-3	The Flowdown of Requirements.	58	Figure 6.5-1	Configuration Management Process	145
Figure 4.3-1	Logical Decomposition Process.	63	Figure 6.5-2	Five Elements of Configuration Management	145
Figure 4.4-1	Design Solution Definition Process	66	Figure 6.5-3	Evolution of Technical Baseline	147
Figure 4.4-2	The Doctrine of Successive Refinement	67	Figure 6.5-4	Typical Change Control Process	148
Figure 4.4-3	A Quantitative Objective Function, Dependent on Life Cycle Cost and All Aspects of Effectiveness.	71	Figure 6.6-1	Technical Data Management Process.	151
Figure 5.0-1	Product Realization	78	Figure 6.7-1	Technical Assessment Process	158
Figure 5.1-1	Product Implementation Process	79	Figure 6.7-2	Planning and Status Reporting Feedback Loop	159
			Figure 6.8-1	Decision Analysis Process	165
			Figure 6.8-2	Risk Analysis of Decision Alternatives	166
			Figure G.1-1	PBS Example	208
			Figure G.3-1	Technology Assessment Process	209
			Figure G.3-2	Architectural Studies and Technology Development	210
			Figure G.4-1	Technology Readiness Levels.	211
			Figure G.4-2	TMA Thought Process	212
			Figure G.4-3	TRL Assessment Matrix.	213

Table of Tables

Table 2.1-1	Alignment of the 17 SE Processes to AS9100	7	Table 6.1-2	Examples of Types of Facilities to Consider during Planning	120
Table 2.2-1	Project Life Cycle Phases	9	Table 6.6-1	Technical Data Tasks	156
Table 2.7-1	NASA System Engineering Competency Model	14	Table 6.7-1	Purpose and Results for Life-Cycle Reviews for Spaceflight Projects . .	161
Table 3.0-1	SE Product Maturity from NPR 7123.1	19	Table 6.8-1	Typical Information to Capture in a Decision Report.	171
Table 3.11-1	Example of Program/Project Types . .	38	Table D-1	Requirements Verification Matrix . .	202
Table 3.11-2	Example of Tailoring NPR 7120.5 Required Project Products	39	Table E-1	Validation Requirements Matrix . . .	204
Table 3.11-3	Example Use of a Compliance Matrix .	41	Table G.1-1	Products Provided by the TA as a Function of Program/Project Phase .	207
Table 4.1-1	Stakeholder Identification throughout the Life Cycle	47	Table J-1	Guidance on SEMP Content per Life-Cycle Phase	233
Table 4.2-1	Benefits of Well-Written Requirements	59	Table K-1	Example of Expected Maturity of Key Technical Plans.	235
Table 4.2-2	Requirements Metadata	59	Table R.2-1	HSI Activity, Product, or Risk Mitigation by Program/Project Phase	250
Table 5.3-1	Example information in Verification Procedures and Reports	94			
Table 6.1-1	Example Engineering Team Disciplines in Pre-Phase A for Robotic Infrared Observatory	118			

Table of Boxes

The Systems Engineer's Dilemma	12	Differences between Verification and Validation Testing.	89
Space Flight Program Formulation	20	Differences between Verification, Qualification, Acceptance and Certification.	90
Space Flight Program Implementation	21	Methods of Verification	93
Space Flight Pre-Phase A: Concept Studies	22	Methods of Validation	101
Space Flight Phase A: Concept and Technology Development	24	Crosscutting Technical Management Keys	114
Space Flight Phase B: Preliminary Design and Technology Completion	26	Types of Hardware	124
Space Flight Phase C: Final Design and Fabrication	28	Environments.	127
Space Flight Phase D: System Assembly, Integration and Test, Launch	30	Definitions	130
Space Flight Phase E: Operations and Sustainment	32	Types of Configuration Management Changes	149
Phase F: Closeout	33	Data Collection Checklist.	155
System Design Keys	44	HSI Relevance	246
Concept of Operations vs. Operations Concept	51	HSI Strategy	246
Example of Functional and Performance Requirements	56	HSI Domains	247
Rationale	60	HSI Requirements	247
Product Realization Keys	78	HSI Implementation	249
		HSI Plan Updates	250



Preface

Since the initial writing of NASA/SP-6105 in 1995 and the following revision (Rev 1) in 2007, systems engineering as a discipline at the National Aeronautics and Space Administration (NASA) has undergone rapid and continued evolution. Changes include using Model-Based Systems Engineering to improve development and delivery of products, and accommodating updates to NASA Procedural Requirements (NPR) 7123.1. Lessons learned on systems engineering were documented in reports such as those by the NASA Integrated Action Team (NIAT), the Columbia Accident Investigation Board (CAIB), and the follow-on Diaz Report. Other lessons learned were garnered from the robotic missions such as Genesis and the Mars Reconnaissance Orbiter as well as from mishaps from ground operations and the commercial space flight industry. Out of these reports came the NASA Office of the Chief Engineer (OCE) initiative to improve the overall Agency systems engineering infrastructure and capability for the efficient and effective engineering of NASA systems, to produce quality products, and to achieve mission success. This handbook update is a part of that OCE-sponsored Agency-wide systems engineering initiative.

In 1995, SP-6105 was initially published to bring the fundamental concepts and techniques of systems engineering to NASA personnel in a way that recognized the nature of NASA systems and the NASA environment. This revision (Rev 2) of SP-6105 maintains that original philosophy while updating the Agency's systems engineering body of knowledge, providing guidance for insight into current best Agency practices, and maintaining the alignment of the handbook with the Agency's systems engineering policy.

The update of this handbook continues the methodology of the previous revision: a top-down compatibility with higher level Agency policy and a bottom-up infusion of guidance from the NASA practitioners in the field. This approach provides the opportunity to obtain best practices from across NASA and bridge the information to the established NASA systems engineering processes and to communicate principles of good practice as well as alternative approaches rather than specify a particular way to accomplish a task. The result embodied in this handbook is a top-level implementation approach on the practice of systems engineering unique to NASA. Material used for updating this handbook has been drawn from many sources, including NPRs, Center systems engineering handbooks and processes, other Agency best practices, and external systems engineering textbooks and guides.

This handbook consists of six chapters: (1) an introduction, (2) a systems engineering fundamentals discussion, (3) the NASA program/project life cycles, (4) systems engineering processes to get from a concept to a design, (5) systems engineering processes to get from a design to a final product, and (6) crosscutting management processes in systems engineering. The chapters are supplemented by appendices that provide outlines, examples, and further information to illustrate topics in the chapters. The handbook makes extensive use of boxes and figures to define, refine, illustrate, and extend concepts in the chapters.

Finally, it should be noted that this handbook provides top-level guidance for good systems engineering practices; it is not intended in any way to be a directive.

NASA/SP-2016-6105 Rev2 supersedes SP-2007-6105 Rev 1 dated December, 2007.

Acknowledgments

The following individuals are recognized as contributing practitioners to the content of this expanded guidance:

Alexander, Michael, NASA/Langley Research Center
Allen, Martha, NASA/Marshall Space Flight Center
Baumann, Ethan, NASA/Armstrong Flight Research Center
Bixby, CJ, NASA/Armstrong Flight Research Center
Boland, Brian, NASA/Langley Research Center
Brady, Timothy, NASA/NASA Engineering and Safety Center
Bromley, Linda, NASA/Headquarters/Bromley SE Consulting
Brown, Mark, NASA/Jet Propulsion Laboratory
Brumfield, Mark, NASA/Goddard Space Flight Center
Campbell, Paul, NASA/Johnson Space Center
Carek, David, NASA/Glenn Research Center
Cox, Renee, NASA/Marshall Space Flight Center
Crable, Vicki, NASA/Glenn Research Center
Crocker, Alan, NASA/Ames Research Center
DeLoof, Richard, NASA/Glenn Research Center
Demo, Andrew/Ames Research Center
Dezfuli, Homayoon, NASA/HQ
Diehl, Roger, NASA/Jet Propulsion Laboratory
DiPietro, David, NASA/Goddard Space Flight Center
Doehne, Thomas, NASA/Glenn Research Center
Duarte, Alberto, NASA/Marshall Space Flight Center
Durham, David, NASA/Jet Propulsion Laboratory
Epps, Amy, NASA/Marshall Space Flight Center
Fashimpaur, Karen, Vantage Partners
Feikema, Douglas, NASA/Glenn Research Center
Fitts, David, NASA/Johnson Space Flight Center
Foster, Michele, NASA/Marshall Space Flight Center
Fuller, David, NASA/Glenn Research Center
Gati, Frank, NASA/Glenn Research Center
Gefert, Leon, NASA/Glenn Research Center
Ghassemieh, Shakib, NASA/Ames Research Center

Grantier, Julie, NASA/Glenn Research Center
Hack, Kurt, NASA/Glenn Research Center
Hall, Kelly, NASA/Glenn Research Center
Hamaker, Franci, NASA/Kennedy Space Center
Hange, Craig, NASA/Ames Research Center
Henry, Thad, NASA/Marshall Space Flight Center
Hill, Nancy, NASA/Marshall Space Flight Center
Hirshorn, Steven, NASA/Headquarters
Holladay, Jon, NASA/NASA Engineering and Safety Center
Hyatt, Mark, NASA/Glenn Research Center
Killebrew, Jana, NASA/Ames Research Center
Jannette, Tony, NASA/Glenn Research Center
Jenks, Kenneth, NASA/Johnson Space Center
Jones, Melissa, NASA/Jet Propulsion Laboratory
Jones, Ross, NASA/Jet Propulsion Laboratory
Killebrew, Jana, NASA/Ames Research Center
Leitner, Jesse, NASA/Goddard Space Flight Center
Lin, Chi, NASA/Jet Propulsion Laboratory
Mascia, Anne Marie, Graphic Artist
McKay, Terri, NASA/Marshall Space Flight Center
McNelis, Nancy, NASA/Glenn Research Center
Mendoza, Donald, NASA/Ames Research Center
Miller, Scott, NASA/Ames Research Center
Montgomery, Patty, NASA/Marshall Space Flight Center
Mosier, Gary, NASA/Goddard Space Flight Center
Noble, Lee, NASA/Langley Research Center
Oleson, Steven, NASA/Glenn Research Center
Parrott, Edith, NASA/Glenn Research Center
Powell, Christine, NASA/Stennis Space Center
Powell, Joseph, NASA/Glenn Research Center
Price, James, NASA/Langley Research Center
Rawlin, Adam, NASA/Johnson Space Center
Rochlis-Zumbado, Jennifer, NASA/Johnson Space Center
Rohn, Dennis, NASA/Glenn Research Center
Rosenbaum, Nancy, NASA/Goddard Space Flight Center

Ryan, Victoria, NASA/Jet Propulsion Laboratory
Sadler, Gerald, NASA/Glenn Research Center
Salazar, George, NASA/Johnson Space Center
Sanchez, Hugo, NASA/Ames Research Center
Schuyler, Joseph, NASA/Stennis Space Center
Sheehe, Charles, NASA/Glenn Research Center
Shepherd, Christena, NASA/Marshall Space Flight Center
Shull, Thomas, NASA/Langley Research Center
Singer, Bart, NASA/Langley Research Center
Slywczak, Richard, NASA/Glenn Research Center
Smith, Scott, NASA/Goddard Space Flight Center
Smith, Joseph, NASA/Headquarters
Sprague, George, NASA/Jet Propulsion Laboratory

Trase, Kathryn, NASA/Glenn Research Center
Trenkle, Timothy, NASA/Goddard Space Flight Center
Vipavetz, Kevin, NASA/Langley Research Center
Voss, Linda, Dell Services
Walters, James Britton, NASA/Johnson Space Center
Watson, Michael, NASA/Marshall Space Flight Center
Weiland, Karen, NASA/Glenn Research Center
Wiedeman, Grace, Dell Services
Wiedenmannott, Ulrich, NASA/Glenn Research Center
Witt, Elton, NASA/Johnson Space Center
Woytach, Jeffrey, NASA/Glenn Research Center
Wright, Michael, NASA/Marshall Space Flight Center
Yu, Henry, NASA/Kennedy Space Center



1.0 Introduction

1.1 Purpose

This handbook is intended to provide general guidance and information on systems engineering that will be useful to the NASA community. It provides a generic description of Systems Engineering (SE) as it should be applied throughout NASA. A goal of the handbook is to increase awareness and consistency across the Agency and advance the practice of SE. This handbook provides perspectives relevant to NASA and data particular to NASA.

This handbook should be used as a companion for implementing NPR 7123.1, Systems Engineering Processes and Requirements, as well as the Center-specific handbooks and directives developed for implementing systems engineering at NASA. It provides a companion reference book for the various systems engineering-related training being offered under NASA's auspices.

1.2 Scope and Depth

This handbook describes systems engineering best practices that should be incorporated in the development and implementation of large and small NASA programs and projects. The engineering of NASA

systems requires a systematic and disciplined set of processes that are applied recursively and iteratively for the design, development, operation, maintenance, and closeout of systems throughout the life cycle of the programs and projects. The scope of this handbook includes systems engineering functions regardless of whether they are performed by a manager or an engineer, in-house or by a contractor.

There are many Center-specific handbooks and directives as well as textbooks that can be consulted for in-depth tutorials. For guidance on systems engineering for information technology projects, refer to Office of Chief Information Officer *Information Technology Systems Engineering Handbook Version 2.0*. For guidance on entrance and exit criteria for milestone reviews of software projects, refer to *NASA-HDBK-2203, NASA Software Engineering Handbook*. A NASA systems engineer can also participate in the NASA Engineering Network (NEN) Systems Engineering Community of Practice, located at <https://nen.nasa.gov/web/se>. This Web site includes many resources useful to systems engineers, including document templates for many of the work products and milestone review presentations required by the NASA SE process.

This handbook is applicable to NASA space flight projects of all sizes and to research and development programs and projects. While all 17 processes are applicable to all projects, the amount of formality, depth of documentation, and timescales are varied as appropriate for the type, size, and complexity of the project. References to “documents” are intended to include not only paper or digital files but also models,

graphics, drawings, or other appropriate forms that capture the intended information.

For a more in-depth discussion of the principles provided in this handbook, refer to the NASA Expanded Guidance for SE document which can be found at <https://nen.nasa.gov/web/se/doc-repository>. This handbook is an abridged version of that reference.

2.0 Fundamentals of Systems Engineering

At NASA, “systems engineering” is defined as a methodical, multi-disciplinary approach for the design, realization, technical management, operations, and retirement of a system. A “system” is the combination of elements that function together to produce the capability required to meet a need. The elements include all hardware, software, equipment, facilities, personnel, processes, and procedures needed for this purpose; that is, all things required to produce system-level results. The results include system-level qualities, properties, characteristics, functions, behavior, and performance. The value added by the system as a whole, beyond that contributed independently by the parts, is primarily created by the relationship among the parts; that is, how they are interconnected.¹ It is a way of looking at the “big picture” when making technical decisions. It is a way of achieving stakeholder functional, physical, and operational performance requirements in the intended use environment over the planned life of the system within cost, schedule, and other constraints. It is a methodology that supports the containment of the life cycle cost of a system. In other words, systems engineering is a logical way of thinking.

Systems engineering is the art and science of developing an operable system capable of meeting requirements within often opposed constraints. Systems engineering is a holistic, integrative discipline, wherein the contributions of structural engineers, electrical engineers, mechanism designers, power engineers, human factors engineers, and many more disciplines are evaluated and balanced, one against another, to produce a coherent whole that is not dominated by the perspective of a single discipline.²

Systems engineering seeks a safe and balanced design in the face of opposing interests and multiple, sometimes conflicting constraints. The systems engineer should develop the skill for identifying and focusing efforts on assessments to optimize the overall design and not favor one system/subsystem at the expense of another while constantly validating that the goals of the operational system will be met. The art is in knowing when and where to probe. Personnel with these skills are usually tagged as “systems engineers.” They may have other titles—lead systems engineer,

1 Eberhardt Rechtin, *Systems Architecting of Organizations: Why Eagles Can't Swim*.

2 Comments on systems engineering throughout Chapter 2.0 are extracted from the speech “System Engineering and the Two Cultures of Engineering” by Michael D. Griffin, NASA Administrator.

technical manager, chief engineer—but for this document, the term “systems engineer” is used.

The exact role and responsibility of the systems engineer may change from project to project depending on the size and complexity of the project and from phase to phase of the life cycle. For large projects, there may be one or more systems engineers. For small projects, the project manager may sometimes perform these practices. But whoever assumes those responsibilities, the systems engineering functions should be performed. The actual assignment of the roles and responsibilities of the named systems engineer may also therefore vary. The lead systems engineer ensures that the system technically fulfills the defined needs and requirements and that a proper systems engineering approach is being followed. The systems engineer oversees the project’s systems engineering activities as performed by the technical team and directs, communicates, monitors, and coordinates tasks. The systems engineer reviews and evaluates the technical aspects of the project to ensure that the systems/subsystems engineering processes are functioning properly and evolves the system from concept to product. The entire technical team is involved in the systems engineering process.

The systems engineer usually plays the key role in leading the development of the concept of operations (ConOps) and resulting system architecture, defining boundaries, defining and allocating requirements, evaluating design tradeoffs, balancing technical risk between systems, defining and assessing interfaces, and providing oversight of verification and validation activities, as well as many other tasks. The systems engineer typically leads the technical planning effort and has the prime responsibility in documenting many of the technical plans, requirements and specification documents, verification and validation documents, certification packages, and other technical documentation.

In summary, the systems engineer is skilled in the art and science of balancing organizational, cost, and technical interactions in complex systems. The systems engineer and supporting organization are vital to supporting program and Project Planning and Control (PP&C) with accurate and timely cost and schedule information for the technical activities. Systems engineering is about tradeoffs and compromises; it uses a broad crosscutting view of the system rather than a single discipline view. Systems engineering is about looking at the “big picture” and not only ensuring that they get the design right (meet requirements) but that they also get the right design (enable operational goals and meet stakeholder expectations).

Systems engineering plays a key role in the project organization. Managing a project consists of three main objectives: managing the technical aspects of the project, managing the project team, and managing the cost and schedule. As shown in [FIGURE 2.0-1](#), these three functions are interrelated. Systems engineering is focused on the technical characteristics of decisions including technical, cost, and schedule and on providing these to the project manager. The Project Planning and Control (PP&C) function is responsible for identifying and controlling the cost and schedules of the project. The project manager has overall responsibility for managing the project team and ensuring that the project delivers a technically correct system within cost and schedule. Note that there are areas where the two cornerstones of project management, SE and PP&C, overlap. In these areas, SE provides the technical aspects or inputs whereas PP&C provides the programmatic, cost, and schedule inputs.

This document focuses on the SE side of the diagram. The practices/processes are taken from NPR 7123.1, NASA Systems Engineering Processes and Requirements. Each process is described in much greater detail in subsequent chapters of this

PROJECT MANAGEMENT

PROJECT MANAGEMENT ACTIVITIES

- Setting up Project Team
- Programmatic Stakeholders (non-technical, non-business)
- Programmatic Planning (non-technical, non-business)
- Identifying Programmatic (non-technical) requirements
- Identifying Programmatic Risks
- Technology Transfer and Commercialization
- Integration of technical and non-technical activities
- Overall Approver/Decider

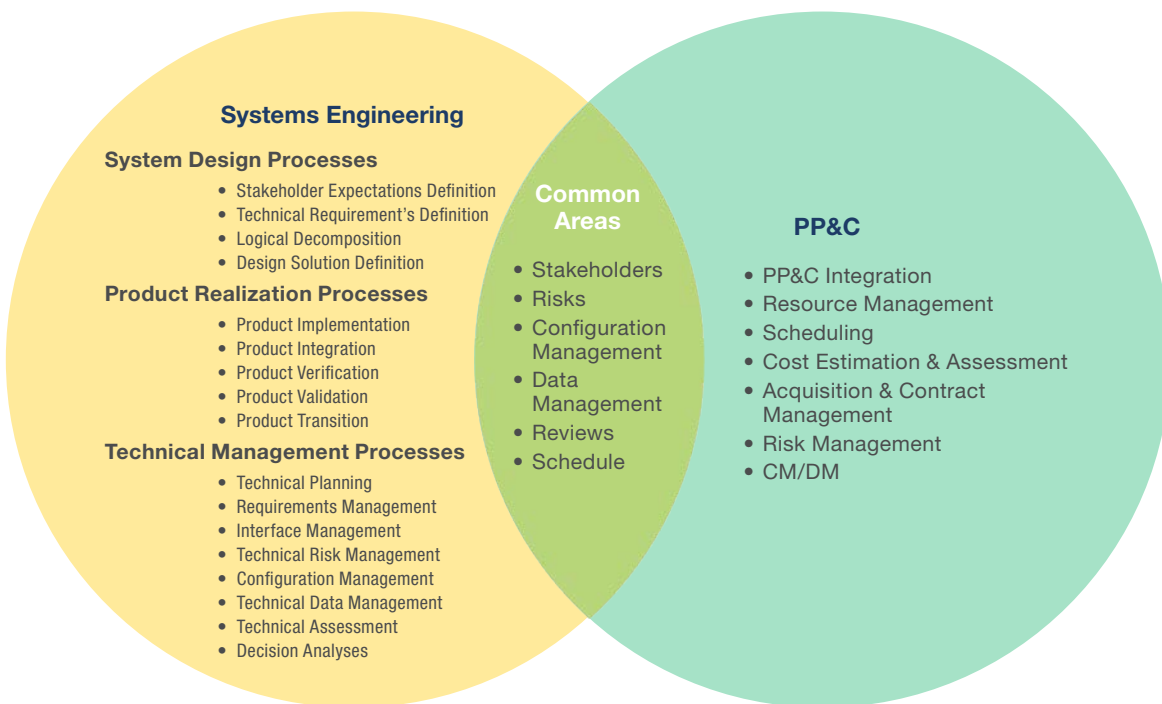


FIGURE 2.0-1 SE in Context of Overall Project Management

document, but an overview is given in the following subsections of this chapter.

2.1 The Common Technical Processes and the SE Engine

There are three sets of common technical processes in NPR 7123.1, NASA Systems Engineering Processes and Requirements: system design, product realization, and technical management. The processes in each set and their interactions and flows are illustrated

by the NPR systems engineering “engine” shown in [FIGURE 2.1-1](#). The processes of the SE engine are used to develop and realize the end products. This chapter provides the application context of the 17 common technical processes required in NPR7123.1. The system design processes, the product realization processes, and the technical management processes are discussed in more detail in [Chapters 4.0, 5.0, and 6.0](#), respectively. Processes 1 through 9 indicated in [FIGURE 2.1-1](#) represent the tasks in the execution of a project. Processes 10 through 17 are crosscutting tools for carrying out the processes.

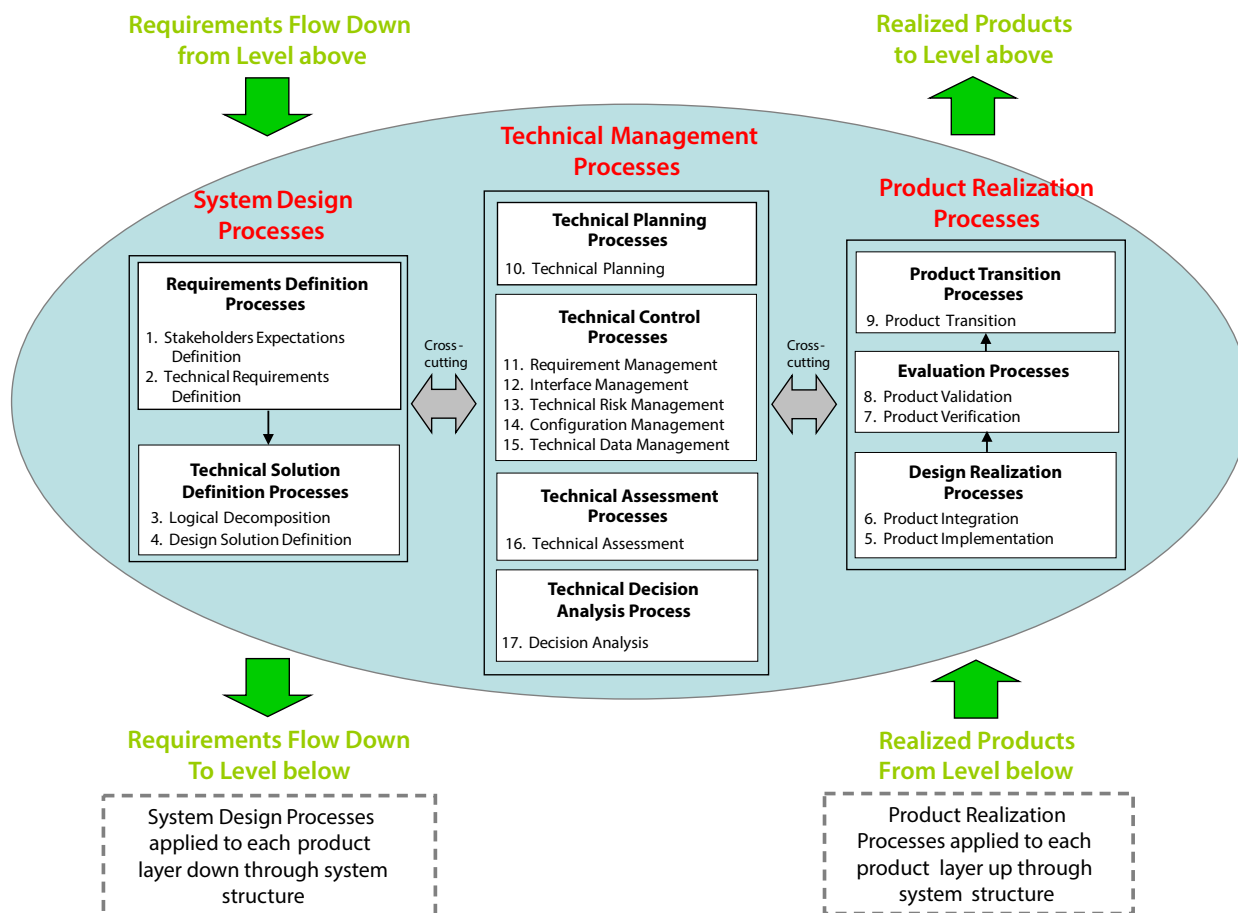


FIGURE 2.1-1 The Systems Engineering Engine (NPR 7123.1)

- System Design Processes:** The four system design processes shown in FIGURE 2.1-1 are used to define and baseline stakeholder expectations, generate and baseline technical requirements, decompose the requirements into logical and behavioral models, and convert the technical requirements into a design solution that will satisfy the baselined stakeholder expectations. These processes are applied to each product of the system structure from the top of the structure to the bottom until the lowest products in any system structure branch are defined to the point where they can be built, bought, or reused. All other products in the system structure are realized by implementation or integration.
- Product Realization Processes:** The product realization processes are applied to each operational/mission product in the system structure starting from the lowest level product and working up to higher level integrated products. These processes are used to create the design solution for each product (through buying, coding, building, or reusing) and to verify, validate, and transition up to the next hierarchical level those products that satisfy their design solutions and meet stakeholder

expectations as a function of the applicable life cycle phase.

- **Technical Management Processes:** The technical management processes are used to establish and evolve technical plans for the project, to manage communication across interfaces, to assess progress against the plans and requirements for the system products or services, to control technical execution of the project through to completion, and to aid in the decision-making process.

The processes within the SE engine are used both iteratively and recursively. As defined in NPR 7123.1, “iterative” is the “application of a process to the same

product or set of products to correct a discovered discrepancy or other variation from requirements,” whereas “recursive” is defined as adding value to the system “by the repeated application of processes to design next lower layer system products or to realize next upper layer end products within the system structure. This also applies to repeating application of the same processes to the system structure in the next life cycle phase to mature the system definition and satisfy phase success criteria.” The technical processes are applied recursively and iteratively to break down the initializing concepts of the system to a level of detail concrete enough that the technical team can implement a product from the information. Then the processes are applied recursively and iteratively to

TABLE 2.1-1 Alignment of the 17 SE Processes to AS9100

SE Process	AS9100 Requirement
Stakeholder Expectations	Customer Requirements
Technical Requirements Definition	Planning of Product Realization
Logical Decomposition	Design and Development Input
Design Solution Definition	Design and Development Output
Product Implementation	Control of Production
Product Integration	Control of Production
Product Verification	Verification
Product Validation	Validation
Product Transition	Control of Work Transfers; Post Delivery Support, Preservation of Product
Technical Planning	Planning of Product Realization; Review of Requirements; Measurement, Analysis and Improvement
Requirements Management	Design and Development Planning; Purchasing
Interface Management	Configuration Management
Technical Risk Management	Risk Management
Configuration Management	Configuration Management; Identification and Traceability; Control of Nonconforming Product
Technical Data Management	Control of Documents; Control of Records; Control of Design and Development Changes
Technical Assessment	Design and Development Review
Decision Analysis	Measurement, Analysis and Improvement; Analysis of Data

integrate the smallest product into greater and larger systems until the whole of the system or product has been assembled, verified, validated, and transitioned.

For a detailed example of how the SE Engine could be used, refer to the NASA Expanded Guidance for SE document at <https://nen.nasa.gov/web/se/doc-repository>.

AS9100 is a widely adopted and standardized quality management system developed for the commercial aerospace industry. Some NASA Centers have chosen to certify to the AS9100 quality system and may require their contractors to follow NPR 7123.1. **TABLE 2.1-1** shows how the 17 NASA SE processes align with AS9100.

2.2 An Overview of the SE Engine by Project Phase

FIGURE 2.2-1 conceptually illustrates how the SE engine is used during each phase of a project (Pre-Phase A through Phase F). The life cycle phases are described in **TABLE 2.2-1**. **FIGURE 2.2-1** is a *conceptual* diagram. For full details, refer to the poster version of this figure, which is located at <https://nen.nasa.gov/web/se/doc-repository>.

The uppermost horizontal portion of this chart is used as a reference to project system maturity, as the project progresses from a feasible concept to an as-deployed system; phase activities; Key Decision Points (KDPs); and major project reviews. The next major horizontal band shows the technical development

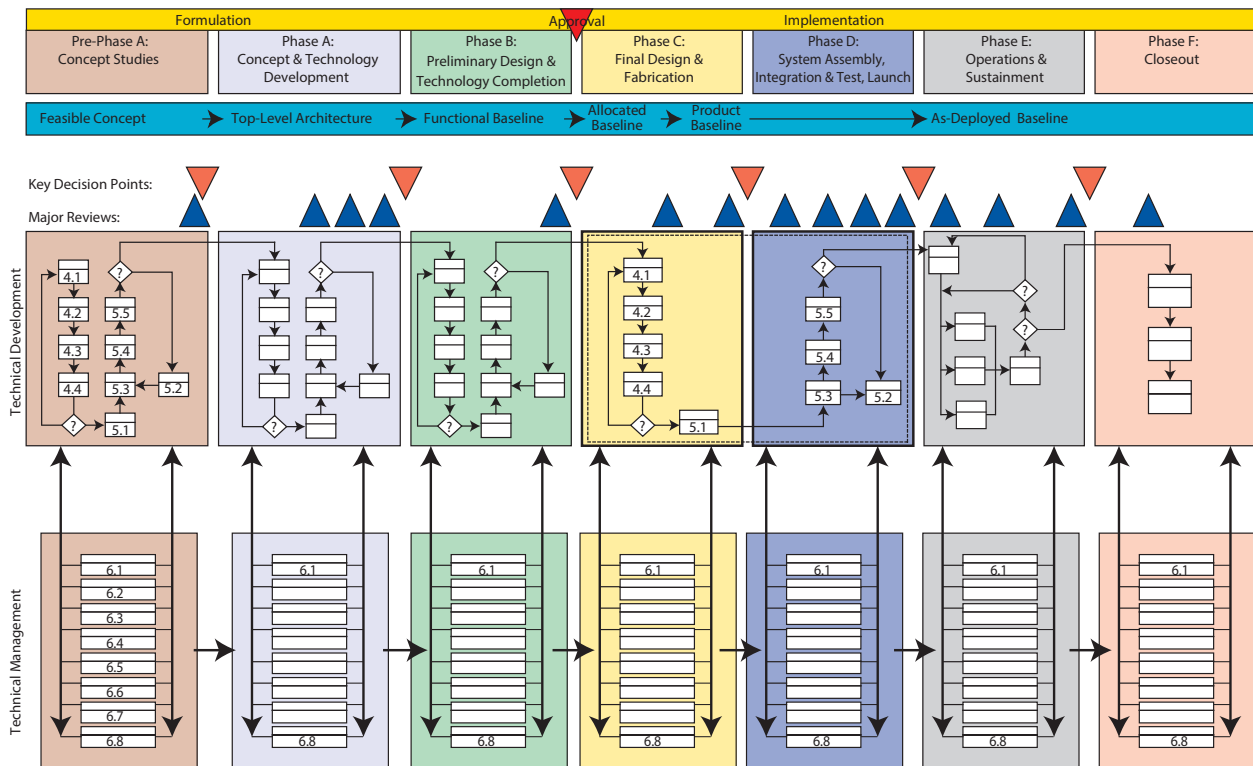


FIGURE 2.2-1 Miniature Version of the Poster-Size NASA Project Life Cycle Process Flow for Flight and Ground Systems Accompanying this Handbook

TABLE 2.2-1 Project Life Cycle Phases

Phase		Purpose	Typical Outcomes
Pre-Formulation	Pre-Phase A Concept Studies	To produce a broad spectrum of ideas and alternatives for missions from which new programs/projects can be selected. Determine feasibility of desired system, develop mission concepts, draft system-level requirements, assess performance, cost, and schedule feasibility; identify potential technology needs, and scope.	Feasible system concepts in the form of simulations, analysis, study reports, models, and mock-ups
	Phase A Concept and Technology Development	To determine the feasibility and desirability of a suggested new system and establish an initial baseline compatibility with NASA's strategic plans. Develop final mission concept, system-level requirements, needed system technology developments, and program/project technical management plans.	System concept definition in the form of simulations, analysis, engineering models and mock-ups, and trade study definition
Formulation	Phase B Preliminary Design and Technology Completion	To define the project in enough detail to establish an initial baseline capable of meeting mission needs. Develop system structure end product (and enabling product) requirements and generate a preliminary design for each system structure end product.	End products in the form of mock-ups, trade study results, specification and interface documents, and prototypes
	Phase C Final Design and Fabrication	To complete the detailed design of the system (and its associated subsystems, including its operations systems), fabricate hardware, and code software. Generate final designs for each system structure end product.	End product detailed designs, end product component fabrication, and software development
Implementation	Phase D System Assembly, Integration and Test, Launch	To assemble and integrate the system (hardware, software, and humans), meanwhile developing confidence that it is able to meet the system requirements. Launch and prepare for operations. Perform system end product implementation, assembly, integration and test, and transition to use.	Operations-ready system end product with supporting related enabling products
	Phase E Operations and Sustainment	To conduct the mission and meet the initially identified need and maintain support for that need. Implement the mission operations plan.	Desired system
	Phase F Closeout	To implement the systems decommissioning/disposal plan developed in Phase E and perform analyses of the returned data and any returned samples.	Product closeout

processes (steps 1 through 9) in each project phase. The SE engine cycles five times from Pre-Phase A through Phase D. Note that NASA's management has structured Phases C and D to “split” the technical development processes in half in Phases C and D to ensure closer management control. The engine is bound by a dashed line in Phases C and D. Once a project enters into its operational state (Phase E)

and closes out (Phase F), the technical work shifts to activities commensurate with these last two project phases. The next major horizontal band shows the eight technical management processes (steps 10 through 17) in each project phase. The SE engine cycles the technical management processes seven times from Pre-Phase A through Phase F.

2.3 Example of Using the SE Engine

In Pre-Phase A, the SE engine is used to develop the initial concepts; clearly define the unique roles of humans, hardware, and software in performing the missions objectives; establish the system functional and performance boundaries; develop/identify a preliminary/draft set of key high-level requirements, define one or more initial Concept of Operations (ConOps) scenarios; realize these concepts through iterative modeling, mock-ups, simulation, or other means; and verify and validate that these concepts and products would be able to meet the key high-level requirements and ConOps. The operational concept must include scenarios for all significant operational situations, including known off-nominal situations. To develop a useful and complete set of scenarios, important malfunctions and degraded-mode operational situations must be considered. The importance of early ConOps development cannot be underestimated. As system requirements become more detailed and contain more complex technical information, it becomes harder for the stakeholders and users to understand what the requirements are conveying; i.e., it may become more difficult to visualize the end product. The ConOps can serve as a check in identifying missing or conflicting requirements.

Note that this Pre-Phase A initial concepts development work is not the formal verification and validation program that is performed on the final product, but rather it is a methodical run through ensuring that the concepts that are being developed in this Pre-Phase A are able to meet the likely requirements and expectations of the stakeholders. Concepts are developed to the lowest level necessary to ensure that they are feasible and to a level that reduces the risk low enough to satisfy the project. Academically, this process could proceed down to the circuit board level for every system; however, that would involve a great deal of time and money. There may be a higher level or tier of product than circuit board level that would

enable designers to accurately determine the feasibility of accomplishing the project, which is the purpose of Pre-Phase A.

During Phase A, the recursive use of the SE engine is continued, this time taking the concepts and draft key requirements that were developed and validated during Pre-Phase A and fleshing them out to become the set of baseline system requirements and ConOps. During this phase, key areas of high risk might be simulated to ensure that the concepts and requirements being developed are good ones and to identify verification and validation tools and techniques that will be needed in later phases.

During Phase B, the SE engine is applied recursively to further mature requirements and designs for all products in the developing product tree and perform verification and validation of concepts to ensure that the designs are able to meet their requirements. Operational designs and mission scenarios are evaluated and feasibility of execution within design capabilities and cost estimates are assessed.

Phase C again uses the left side of the SE engine to finalize all requirement updates, finalize the ConOps validation, develop the final designs to the lowest level of the product tree, and begin fabrication.

Phase D uses the right side of the SE engine to recursively perform the final implementation, integration, verification, and validation of the end product, and at the final pass, transition the end product to the user.

The technical management processes of the SE engine are used in Phases E and F to monitor performance; control configuration; and make decisions associated with the operations, sustaining engineering, and closeout of the system. Any new capabilities or upgrades of the existing system reenter the SE engine as new developments.
